

House Release Walkthrough

How a stage release is actually done in MarkSystems — built from a screen recording captured 9/22/2026, releasing house 00100165 (Sabana Reserve, model MO6/TRA).

This document exists to make step 2 of the Procurement & Release Control page's "How to use this page" guidance concrete. It was rebuilt from a second, clearer recording that captured the dialogs the first one missed — several details below correct what an earlier version of this document guessed at from text-only step descriptions.

1. Log in and select the company

Log into MarkSystems, then use the Company Selection dialog to pick the company the house belongs to.

2. Find the house and open Create Work Orders


Scroll the House Release grid to find the target house, then double-click its row. This opens a **Create Work Orders** window for that specific house (in the recording: "Create Work Orders – 00100165").

Confirm the relevant field to proceed — this is what tells MarkSystems to start generating work orders for every budgeted cost code on this house for the stage being released.


3. Duplicate Contracts Found — pick the vendor contract

For any cost code where more than one active vendor contract exists, MarkSystems stops and shows a **Duplicate Contracts Found** dialog listing every eligible contract for that cost code — vendor, amount, and whether it was the *Previous* vendor used for this cost code. You pick the correct one and click Select. This repeats once per cost code that has more than one eligible contract; below are two different examples from the same release.

Correction from an earlier version of this document: this dialog does **not** mean "a duplicate already exists, do you want another one." It's a contract-selection step — MarkSystems is asking which vendor's contract should price this cost code, because more than one qualifies. The real risk it points at is different: if the wrong contract gets selected here, or the same cost code ends up split across two separate work orders on different contracts, that produces exactly the pattern seen repeatedly in the manual duplicate-payments check log (houses 00400236, 00400175, etc.) — two work orders on the same cost code, different vendors, different amounts. That's the gap the Procurement & Release Control page's own Duplicate flag is built to catch after the fact.

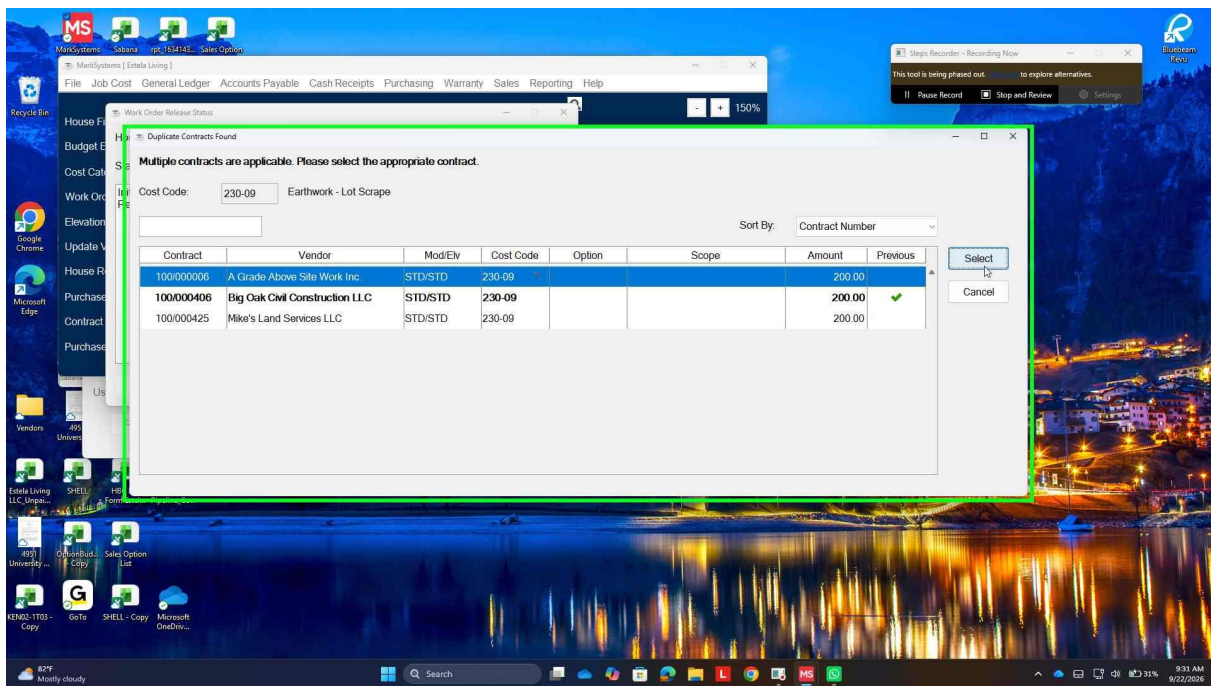


Cost code 230-09 (Earthwork – Lot Scrape): 3 eligible contracts at the same \$200.00 amount; 2 are marked as Previous.

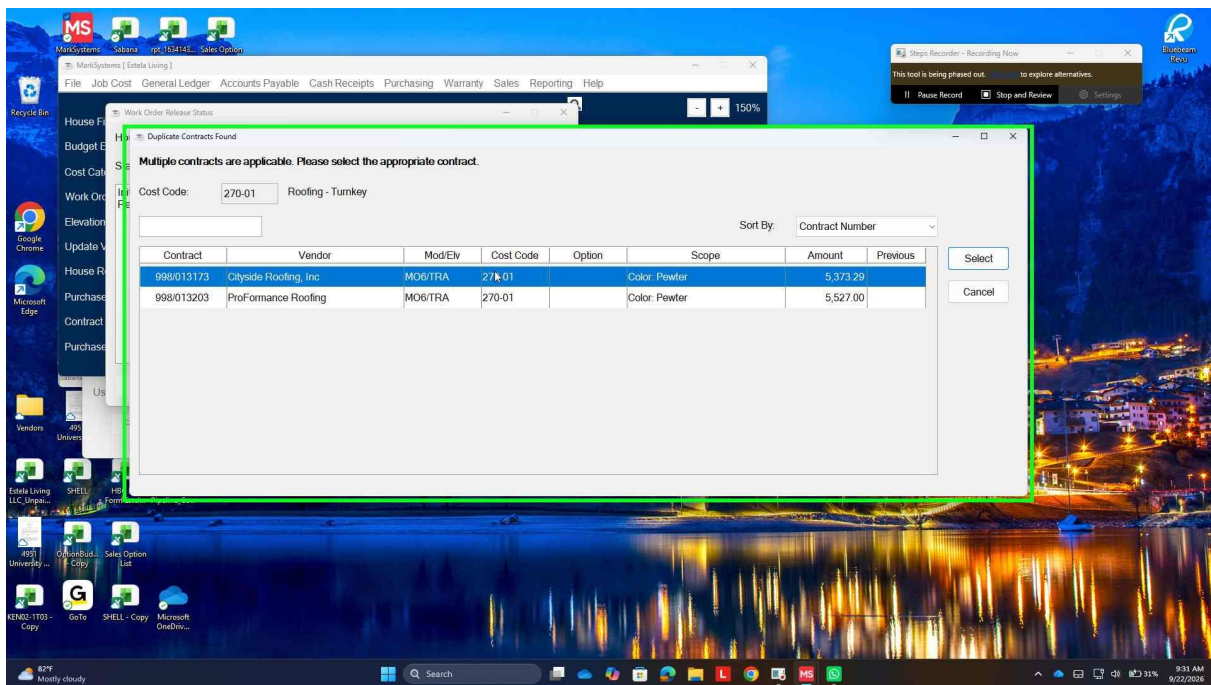

Cost code 270-01 (Roofing – Turnkey): 2 eligible contracts at meaningfully different amounts (\$5,373.29 vs \$5,527.00) — picking the wrong one here has a real budget impact.

4. Price Option, then review the list before previewing

MarkSystems asks a simple yes/no — **Price Option: "Show prices on work orders?"** — behind it, the **Work Order Release Status** window has already been listing every work order it's about to create, one line per cost code ("Preview Work Order (X) created for cost code Y"). That window has three real choices at the bottom: **Preview**, **Create**, or **Cancel**.

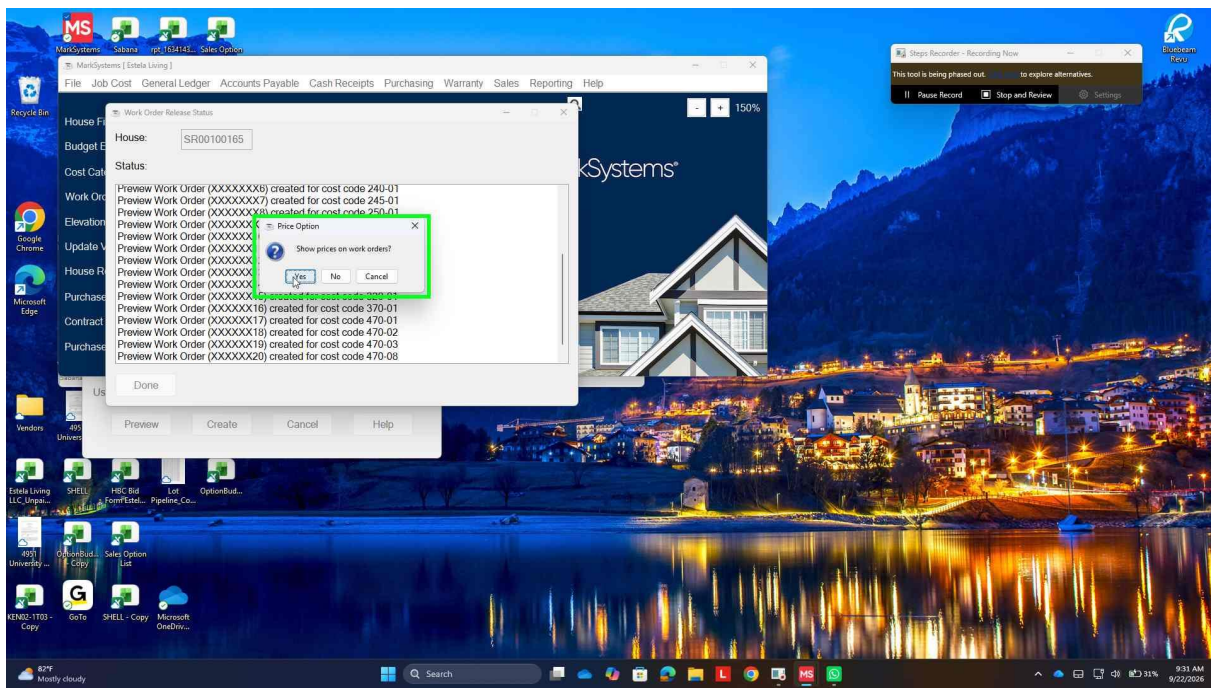


The Work Order Release Status list (cost codes 240-01 through 470-08 shown) with the Price Option prompt on top.

Both recordings captured so far went down the **Preview** path, which opens a read-only PDF and does not finalize anything. Actually finalizing the release means coming back to this same screen and clicking **Create** instead — that step hasn't been recorded yet, so treat this document as covering everything up through the preview, not the final confirmation.

5. Preview — one page per work order

Clicking Preview opens a PDF in Adobe Acrobat with one page per work order about to be created — 20 pages in this recording, each still marked **(PREVIEW)** in the work order number until the batch is actually created.

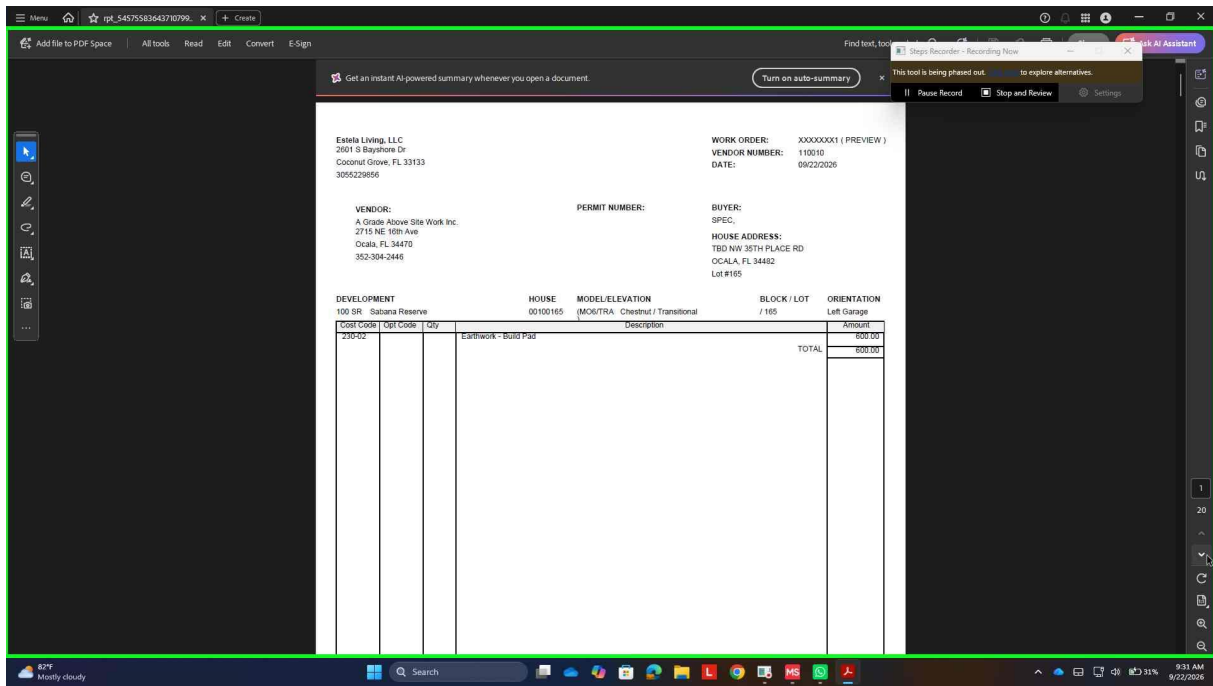

Page 1 of 20 — cost code 230-02, Earthwork – Build Pad, \$600.00

How this maps to the Procurement & Release Control page

In MarkSystems...	...use this page to...
Decide a house is due for a stage release	Check the Release Queue tab first — it tells you exactly which stage is due, computed live from the permit tracker / house release schedule, before you go do anything in MarkSystems
Pick a contract in Duplicate Contracts Found	No equivalent here — this is a MarkSystems-side pricing decision. But if the wrong contract gets picked (or a cost code ends up on two separate work orders), that's exactly what shows up as a Duplicate flag here afterward
Create → work orders actually get made	Click "Review released WOs" on that house's row to see those same work orders reconciled against budget, with duplicates and amount mismatches flagged automatically
Job-specific cost codes on the preview (driveway, septic, grading, etc.)	Use the Job-Specific filter in Reconciliation — those depend on lot size/drawings, not a fixed budget, so they get their own "matches drawings/site" checkbox instead of an amount-based flag

Source: Windows Steps Recorder capture, 9/22/2026 9:29:26 AM – 9:31:45 AM (50 recorded steps), replacing an earlier 9/21/2026 recording of the same house that lacked screenshots of the Duplicate Contracts Found and Price Option dialogs. The full recording, including screenshots not reproduced here, is available as house-release-recording.zip on the Procurement & Release Control page.
